

U.S. Army Corps of Engineers Project Update

7/16/2019

(DATES AND PROJECTS SUBJECT TO CHANGE)

Ongoing contracts/mods:

- 1) Sims to Turning Basin (Crosby Dredging, LLC): Work is complete. Dredge has left the area and the Contractor is demobilizing from the placement area.
- 2) Spilman PA Containment Dike Raise: (Apollo Environmental Strategies Inc); work is ongoing. Work is expected to complete in October 2019.
- 3) Freeport Harbor PA1 Dike Raising (Herve Cody): Work is ongoing. Estimated completion is December 2019.
- 4) HSC PA14 and 15 Dewatering (Wilco Marsh Buggies, Inc): Work is complete.
- 5) GIWW FY18 Freeport to Upper Matagorda with Options for San Bernard dredging and Colorado River Dredging (Callan Marine): Dredge General Patton finished Channel to Palacios, conducted some private work, and will be resuming work on the Colorado River, Colorado River Crossing, GIWW, and San Bernard River. Overall contract completion expected December 2019.
- 6) HSC Morgan's to Exxon and Barbours Flare Dredging (Orion Marine Group): In process of issuing modification to address draft restriction at Barbours Cut.
- 7) HSC Alexander PA Improvements (Affolter Contracting, Inc): Work ongoing. Completion expected Dec 2019.
- 8) Galveston Pelican Island PA Improvements (RLB Contracting, Inc): Work ongoing. Completion estimated March 2020.
- 9) Brazos River Floodgates and Colorado River Locks Scour Hole Repairs: awarded April 2019 to Pontchartrain Partners, LLC. Contractor is currently procuring materials. Work is anticipated to begin at the Colorado River Locks in September 2019. We anticipate approximately two months of work at the CRL, then the Contractor will move on to the BRFG for an additional two months of work.
- 10) Galveston Entrance Channel and HSC Bolivar to Redfish Hopper dredging: Awarded June 18 2019. VTS Pre-Dredging safety coordination meeting being held 7/16/19 at 1000 at VTS Houston. Additional info regarding pipeline routes for beach placement will be relayed to Lone Star Boater Rep.


Upcoming Federal projects:

- Bayport Channel Emergency Dredging: P&S developed, requesting approval for reduced advertisement. Anticipate mid-August award.
- HSC Redfish to Beacon 78 and Bayport Flare (hopper dredging): Bids opened, August 2019 award, anticipated start Oct 2019.
- Freeport Jetty and Inside Channel: Aug 2019 award
- HSC Brady Island to Turning Basin: Advertised, August 2019 award
- GIWW Freeport to Upper Matagorda Bay; August 2019 award
- HSC Peggy Lake Dewatering and Dike Raise: Sept 2019 award
- Galveston San Jacinto PA Improvements: Sept 2019 award
- HSC Clinton PA improvements: Sept 2019 award
- HSC Placement Area 14 Dike Raise: Sept 2019 award

- GIWW High Island to Rollover; Bolivar Flare; Channel to Port Bolivar: Sept 2019 award
- Texas City PA Improvements: Sept 2019 Award
- HSC Lost Lake PA Improvements: Delayed, January 2020 award
- HSC Mid Bay PA Improvements: Delayed, Feb 2020 award

Reports of Unsafe Moorings

(Slack Lines as of 07/15/19)

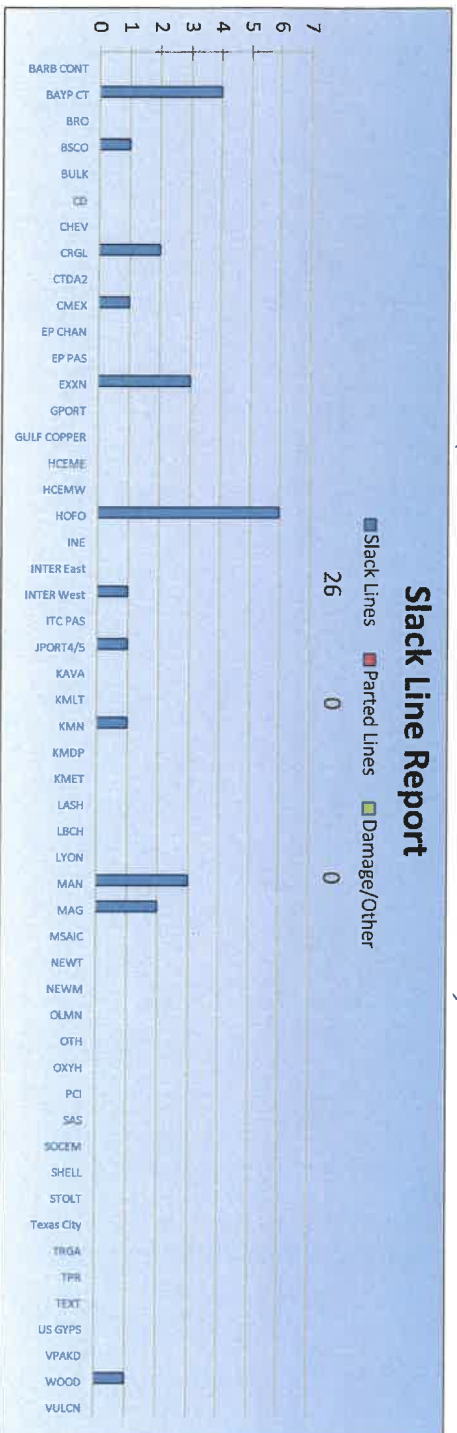

2019 Incidents Summary-7/15/19

	Propulsion	Steering	Generator	Electronic	Grounding	Allision	Collision	Pollution
Ship	3	1				2	3	
Tow					4			2
OSV/Etc								



3 ship/tow collisions and 2 tow/tow collisions



Our 1st parted lines

U.S. Department of Homeland Security
United States Coast Guard

Facility Ready for Inspection

Entered into Spreadsheet

Forwarded to Facilities Unit

Above this line for USCG/MTSRU use only

Facility Self-Assessment Checklist Sector Houston-Galveston

Date Completed:	
Facility Name:	
Address (Street, City, Zip):	
Point of Contact:	
Contact Number(s):	
E-mail Address(es):	
Dock(s):	

An asterisk (“*”) is listed by each item that represents a potential issue. If your answer coincides with the asterisk, please provide additional details in the comments section to describe the current situation and your plans to manage the situation created by the issue.

1. Firefighting			
a. Dock/Facility firefighting systems are fully operational	Yes	No*	N/A*
b. Mutual aid/municipal firefighting support is fully available	Yes	No*	N/A*
Comments:			

2. Medical Services			
a. On-site or community medical services are available, including transport and E/R services	Yes	No*	N/A*
Comments:			

3. Security			
a. Perimeter fencing is intact and entryways/gates secured or manned	Yes	No*	N/A*
b. Available means for 24-hour monitoring of security	Yes	No*	N/A*
c. Available for 24-hour access control	Yes	No*	N/A*
Comments:			

4. Soundings			
a. Soundings taken to identify submerged objects	Yes	No*	N/A*
b. Soundings taken to identify shoaling	Yes	No*	N/A*
c. Soundings include berth and entrance channel to your facilities	Yes	No*	N/A*
d. Controlling depth for each facility based on soundings taken	Enter depth in feet:		
Comments:			

5. Facility Services			
a. Key facility utilities are operational, including power, nitrogen, air and water (as appropriate).	Yes	No*	N/A*
b. Oil/HAZMAT response services (on-site and/or through an OSRO if required) are confirmed available	Yes	No*	N/A*
Comments:			

6. Facility Integrity			
a. The integrity of all MTR transfer systems has been confirmed.	Yes	No*	N/A*
b. All alert/warning systems are tested and operational.	Yes	No*	N/A*
c. Integrity/operation of all mooring systems and dock structure confirmed.	Yes	No*	N/A*
d. Facility is in compliance with all other aspects of their Facility Operations Manual.	Yes	No*	N/A*
Comments:			

7. Vessel Accountability:			
a. Security interface is maintained:	Yes	No*	N/A*
b. Damage to dock and mooring areas:	Yes	No*	N/A*
Comments:			

8. Expected dates/time:	
c. Ready for cargo transfers to begin:	
d. Ready for inspection by USCG facility inspectors:	
Comments:	

9. Other comments:

Please e-mail your completed form to the following e-mail address:
houstonfac@uscg.mil
 For questions, please call the Sector Facilities Branch at 281-464-4767
